

## **Keenan Elementary and Oak Hills Jr High School Monthly Project Update #07 – Through July 2016**

### **Project Site**


- o Primary Electrical Duct Bank is complete
- o Site Lighting Foundations and Pole Standards are being locate, drilled, and poured
- o Stabilization underway for remaining Site Paving



### **Oak Hills Jr High School**

- o Chillers and majority of Mechanical Equipment have been delivered
- o CMU Walls are 95% constructed
- o Steel Erection complete, Detailing of Erected Steel is 90% complete
- o Overhead and Inwall MEP Rough-ins are installing throughout building
- o Spray-on Fireproofing 75% complete and continuing through building
- o Wood Blocking associated with Roof Edge is underway
- o Exterior Damp Proofing underway
- o Interior Metal Stud Framing is ongoing in Sections 1, 2, 8, and 9



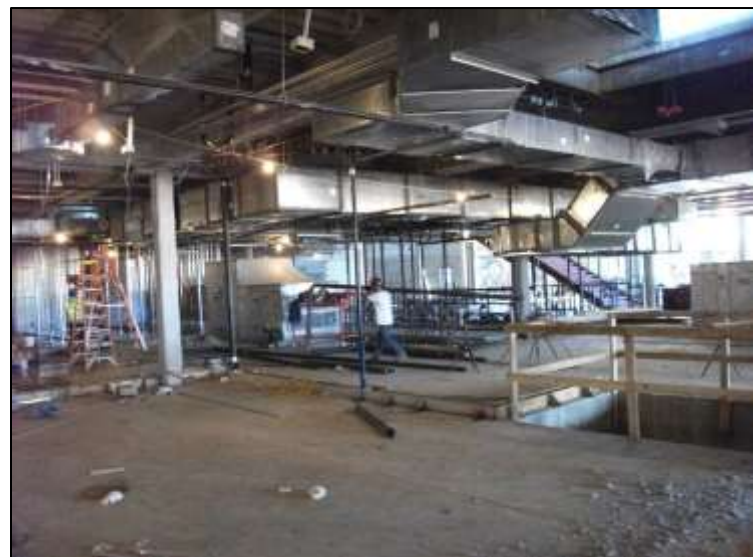



## Keenan Elementary School

- Concrete poured at Stage and Mechanical Mezzanine
- Steel Detailing and Decking 95% complete in Sections 1 – 5
- Damp Proofing complete in Section 1
- Exterior Veneer Face Brick underway
- Roofing scope of work has begun at Sections 1 – 3
- MEP Rough-ins above ceiling in Sections 1 and 2 are 75% complete
- Interior Metal Stud Wall Framing is complete in Sections 1 and 2



